

Georgia Tech Potential Project Flow


Select a period to highlight at right. A legend describing the charting follows.

Revised 4/9/20

Period Highlight: 1

Plan Duration Actual Start % Complete Actual (beyond plan) % Complete (beyond plan)

ACTIVITY	PLAN START	Dept.	Lab PI	Floor	Section	Week	PLAN DURATION	PERCENT COMPLETE	PERIODS
									1 2 3 4 5 6 7 8 9 10 11 12 13 14 15 16 17 18 19 20 21 22 23 24 25 26 27 28 29 30 31 32 33 34 35 36 37 38 39 40 41 42 43 44 45 46 47 48 49 50 51 52 53 54 55 56 57 58 59 60
Kick-Off	1			O'KEEFE	N/A	7/19/2019	1	100%	
Mobilization	2			O'KEEFE	N/A	8/5/2019	3	100%	
ES&T SECOND FLOOR									
ABM TEL (Lab 2315)	5	ChBE	Jones-Group	2	A	8/12/2019	1	100%	
ABM TEL Lab 2321 & 2325-Refresh	5	CEE	Kostas	3	A	8/12/2019	1	0%	
ABM TEL Lab 2305 & 2309	6	ChBE	Rousseau-Group	2	A	9/1/2019	1	100%	
ABM TEL Lab 2321	7	ChBE	Hu-Group	2	A	8/26/2019	1	100%	
ABM TEL Lab 2325	8	ChBE	Jones-Group	2	A	8/19/2019	1	100%	
ABM TEL Lab 2335	9	ChBE	Reichmanis-Group	2	A	9/9/2019	1	100%	
ES&T Lab 2350 & 2355	10	ChBE	2350 (Bahmia); 2355 (Eckert/Liotta)	2	A	9/16/2019	1	100%	
ES&T Lab 2365	11	ChBE	Lively-Group	2	A	9/23/2019	1	100%	
ES&T Lab 2375 & 2380	12	ChBE	Eckert/Liotta-Group	2	A	9/30/2019	1	100%	
ES&T Lab 2385	13	ChBE	Nair-Group	2	A	10/7/2019	1	100%	
ES&T Lab 2107 & 2383	13	EAS;OSE / ChBE	2107 (Weber); 2383 (Eckert/Liotta)	2	A	10/7/2019	1	100%	
ES&T Lab 2115 & 2121	14	EAS;OSE	2115 (Weber); 2121 (Tang)	2	E	10/14/2019	1	100%	
ES&T Lab 2125 & 2131	15	EAS;OSE	2125 (Ingall); 2131 (ingall)	2	E	10/21/2019	1	100%	
ES&T Lab 2150 & 2155	16	Biology	2150 (Weissburg); 2155 (Ratcliff)	2	E	10/28/2019	1	100%	
ES&T Lab 2165	17	Biology	2165 (Kubanek)	2	E	11/4/2019	1	0%	
ES&T Lab 2175 & 2180, 2185	18	Biology	2175 (Kubanek); 2180 & 2185 (Hay)	2	E	11/11/2019	1	0%	
ES&T 2nd Floor As-Built, Docs	20			2	A&C	11/18/2019	5	0%	
ES&T 2nd Floor Drawing Review & Finalization	25			2	A&C	12/23/2019	2	0%	
ES&T Lab L1309 & L1315	19	ATDC	L1309 (Mieron); L1315 (Microplex/ Sophia Biosciences)	L1	A	11/18/2019	1	0%	
ES&T Lab L2150, L2155 & L1325	23	ATDC	L2150 & L2155 - Vacant L1325 - Lena Bioscience & Glympse Bio	L1	A	1/27/2020	1	0%	
ES&T Lab L1160	23	EAS;OSE / ChBE	L1160 (Process Control Lab (Ben Galfond))	L1	E	12/9/2019	1	0%	
ES&T Lab L1155	23	EAS;OSE / ChBE	L1155 (Meg Grantham)	L1	E	12/9/2019	1	0%	
ES&T L1 Floor As-Built, Docs	26			L1	A & C	12/9/2019	5	0%	
ES&T L1 Floor Drawing Review & Finalization	31			L1	A & C	1/13/2020	2	0%	
ES&T L2 FLOOR									
ES&T Lower Level 2	26			L2	A&C	1/27/2020	9	0%	
ES&T Lab L2305	26	Chemistry	Elayne Ashley	L2	A	12/16/2019	1	0%	
ES&T Lab 2311 (Rock-Cutting Lab)	26	COS	Ferrier-Group / Cobb-Group	L2	A	2/3/2020	1	0%	
ES&T Lab 2365 (Machine Shop)	26	ChBE	Jeff Andrews & Brad Parker	L2	A	2/10/2020	1	0%	
ES&T Lab L2102 (Room-Controllers)	26	EAS;OSE	Tang	L2	E	2/3/2020	1	0%	
ES&T Lab L2107, L2115	27	Chemistry	2107 Fernandez L2115 Bahmia	L2	E	1/6/2020	1	0%	
ES&T Lab L2121 & L2125	28	Chemistry	2121 Stockton 2125 Fernandez	L2	E	1/13/2020	1	0%	
ES&T Lab L2131, L2137 & L2139 & L2135 (lab controller only)	29	Chemistry	Fernandez	L2	E	1/20/2020	1	0%	

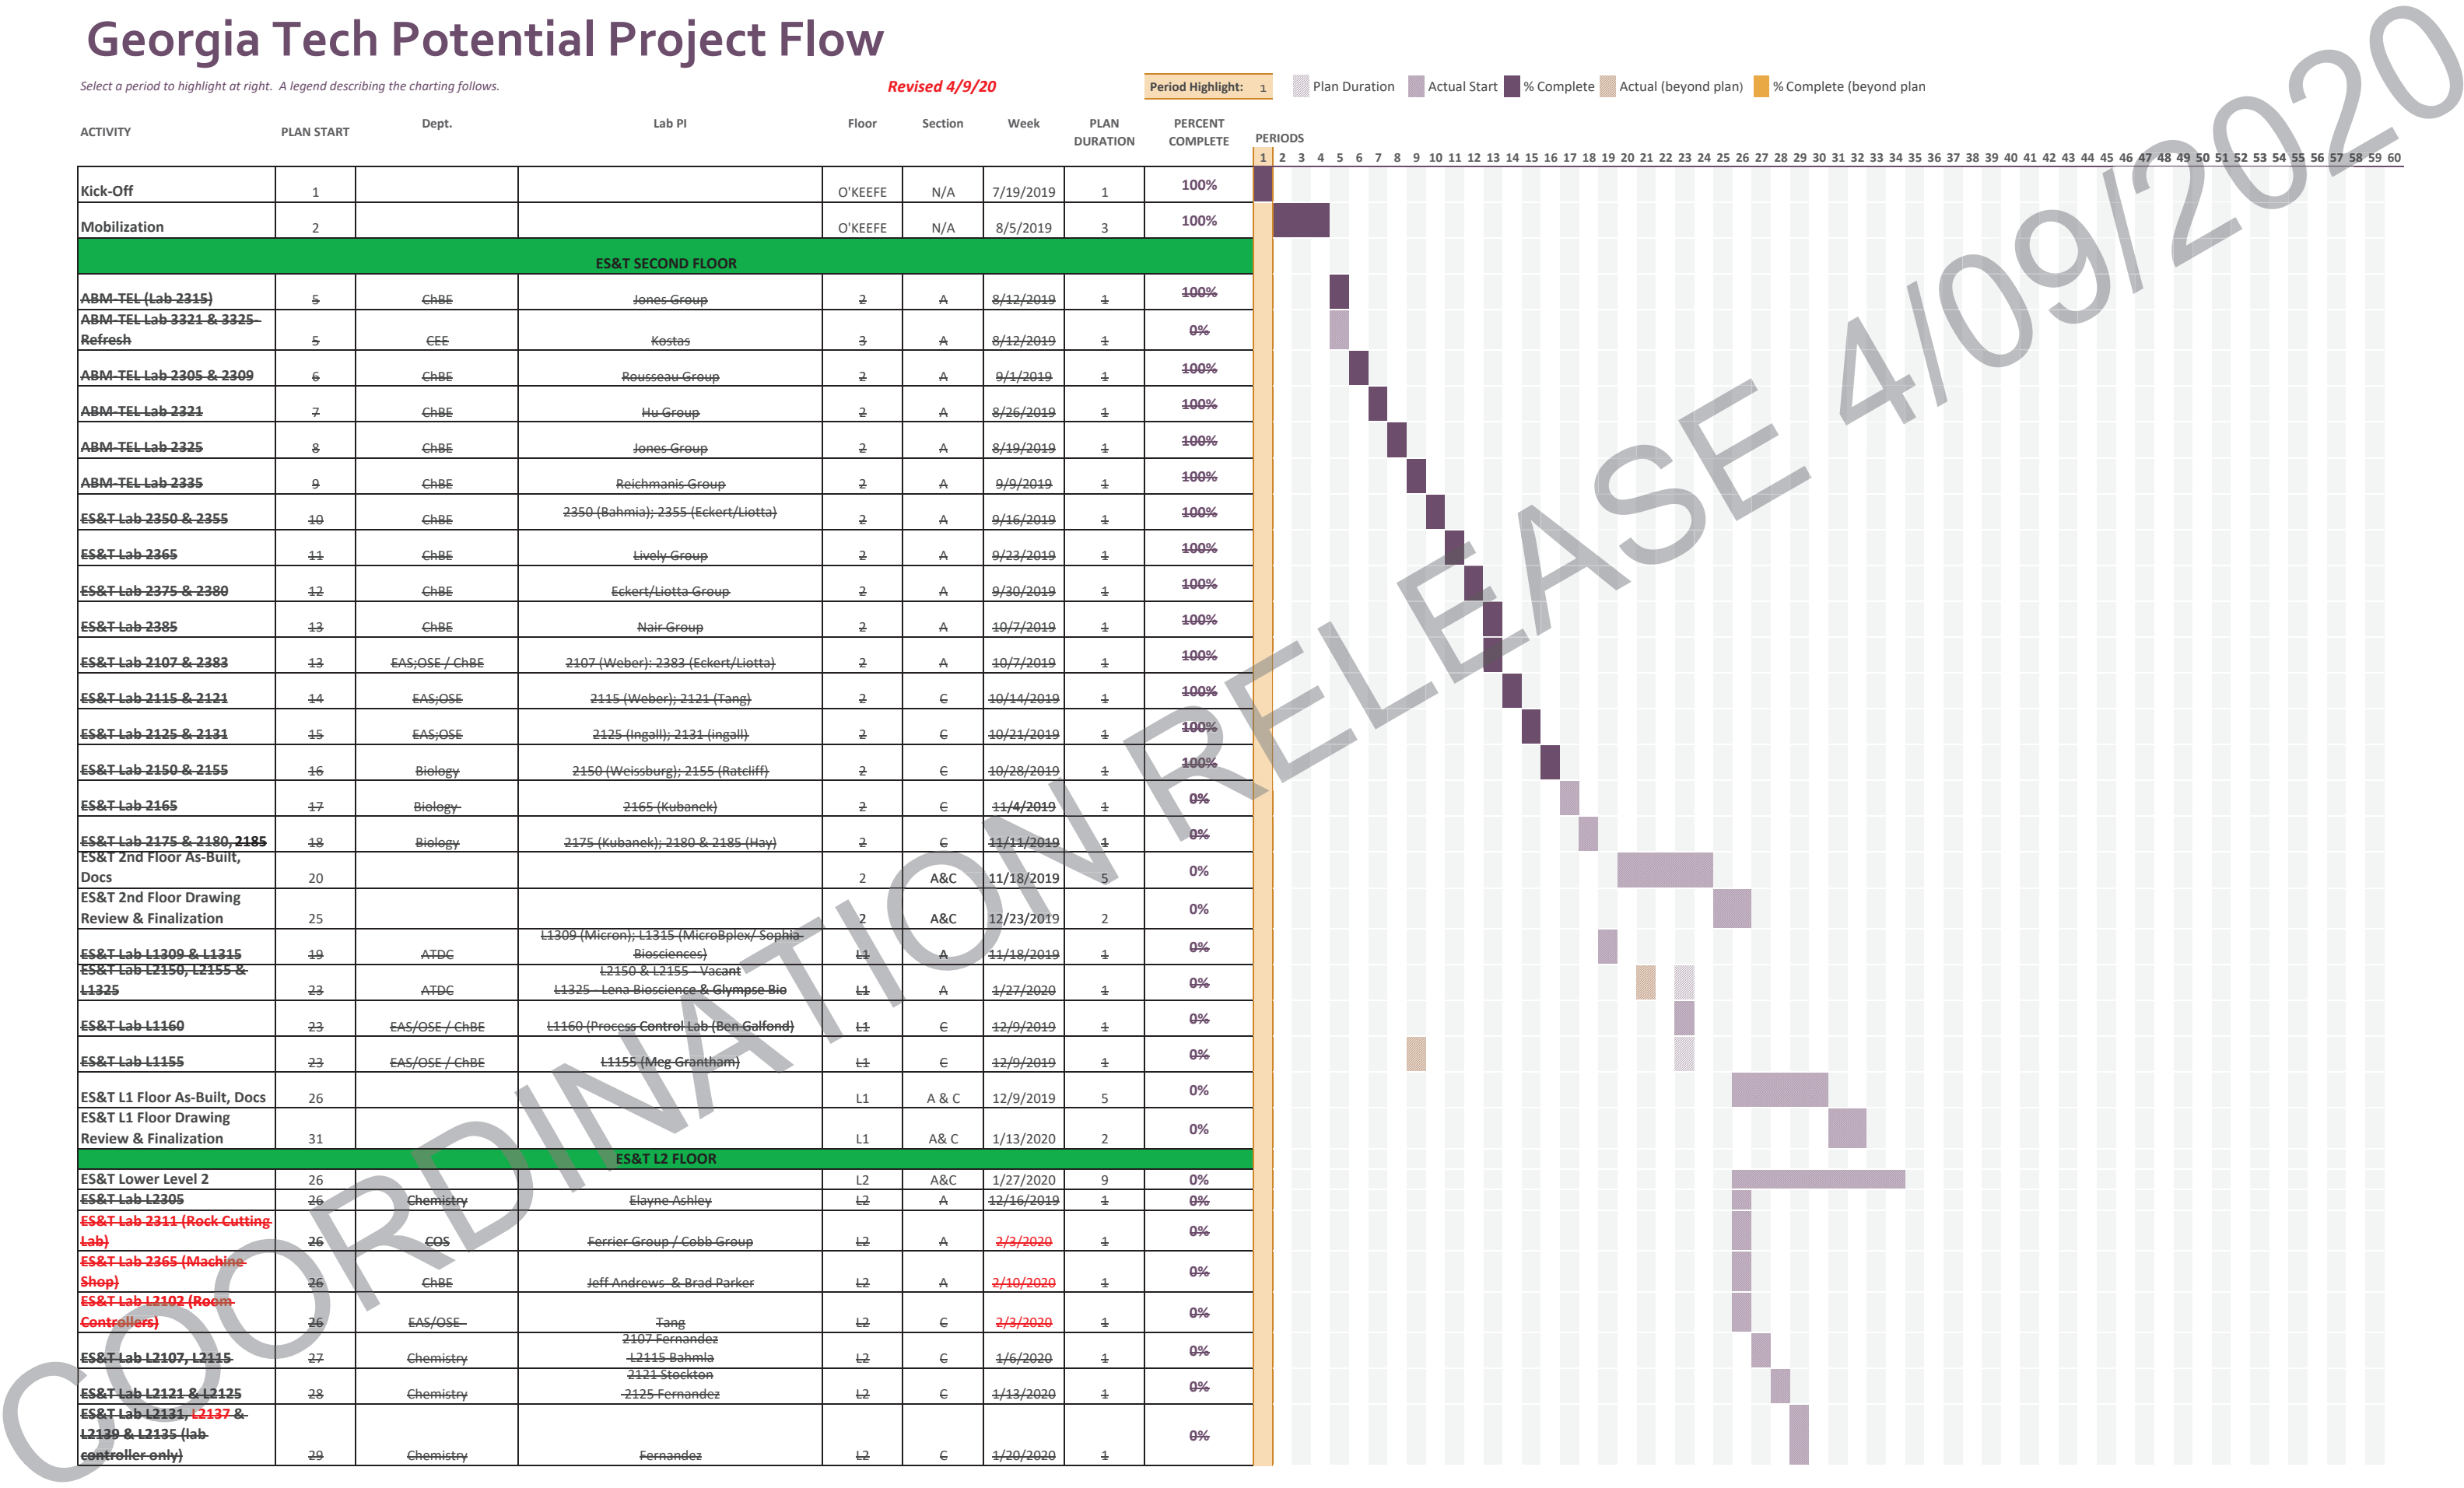

ACTIVITY	PLAN START	Dept.	Lab PI	Floor	Section	Week	PLAN DURATION	PERCENT COMPLETE	PERIODS
									1 2 3 4 5 6 7 8 9 10 11 12 13 14 15 16 17 18 19 20 21 22 23 24 25 26 27 28 29 30 31 32 33 34 35 36 37 38 39 40 41 42 43 44 45 46 47 48 49 50 51 52 53 54 55 56 57 58 59 60
ES&T Lab L2150, L2155 & L1325	30	Chemistry	2150 Weissburg 2155 (N/A) L1325 Lena Bioscience/Glympse Bio	L2	E	1/27/2020	1	0%	
ES&T Office L2165, L2170 (Space Controller)	31	EAS/OSE	Schmidt Group	L2	G	11/4/2019	1	0%	
ES&T L2 Floor As-Built, Docs	36			L2	A	11/11/2019	5	0%	
ES&T L2 Floor Drawing Review & Finalization	41			L2	A	12/16/2019	2	0%	
ES&T Lab L2365	32	Biology, EAS	Machine Shop 1315 Hess	1	A	2/10/2020	1	0%	
ES&T Lab 1315, 1321, 1325	37	ChBE	1321 Cheung 1335 Nair	1	A	2/17/2020	1	0%	
ES&T Lab 1335, L1355 & L1305	33	ChBE	L1355 Diagnostic Solutions/Bionary Scientific L1305 Carbee	1	A	2/24/2020	1	0%	
ES&T Lab 1351, 1355 & 1365	34	ChBE	1351 Cheung 1355 Lively 1365 Meredith	1	A	3/2/2020	1	0%	
ES&T Lab 1107, 1137, 1139 & 1115	35	EAS, OSE / Biology	1107, 1137 & 1139 Taillefert 1115 DiChristina	1	G	3/9/2020	1	0%	
ES&T Lab 1121, 1125 & 1135	36	Biology	1121 Stewart 1125 & 1135 Montoya 1150 Cobb	1	G	3/16/2020	1	0%	
ES&T Lab 1150 & 1185	37	EAS, OSE	1185 Lynch-Stieglitz	1	G	3/23/2020	1	0%	
ES&T Lab 1166	38	ChBE	1166 Glass	1	G	3/30/2020	1	0%	
ES&T First Floor As-Built, Docs	40			First		4/6/2020	5	0%	
ES&T First Floor Drawing Review & Finalization	45			First		5/11/2020	2	0%	
ES&T THIRD FLOOR									
ES&T 3305	40			3	A	4/6/2020	1	0%	
ES&T Lab 3309 & 3315	41	CEE	3309 Xie 3315 Zhu	3	A	4/6/2020	1	0%	
ES&T Lab 3321, 3325, 3335	42	CEE	Kostas/Brown	3	A	4/13/2020	1	0%	
ES&T Lab 3351 & 3353	43	CEE	Pavlostathis	3	A	4/20/2020	1	0%	
ES&T Lab 3355 & 3371	44	CEE	3355 Pavlostathis 3371 Brown	3	A	4/27/2020	1	0%	
ES&T Lab 3375 & 3387	45	ChBE	3375 Jones 3387 Zhu	3	A	5/4/2020	1	0%	
ES&T Lab 3107 & 3115	46	CEE	3107 Kaiser 3115 Fan	3	A	5/11/2020	1	0%	
ES&T Lab 3121 & 3125	47	EAS/OSE	Huey	3	A	5/18/2020	1	0%	
ES&T Lab 3131, 3137, 3139	48	EAS/OSE	3131 (Glass) Ferrier 3137 Taillefert 3139 Lynch-Stieglitz	3	A	5/25/2020	1	0%	
ES&T Lab 3150 & 3155 & 3165	49	CEE / EAS, OSE / EAS, ChBE	3150 Brown 3155 Nenes 3165 Ng	3	A	6/1/2020	1	0%	
ES&T Lab 3171 & 3175	50	EAS	3171 Wine 3175 Robel/ Chu	3	A	6/8/2020	1	0%	
ES&T 3180	50	EAS/OSE	Rienhard	3	A	6/8/2020	1	0%	
ES&T Third Floor As-Built, Docs	52			Third	A	6/15/2020	5	0%	
ES&T Third Floor Drawing Review & Finalization	57			Third		7/20/2020	2	0%	
ES&T FOURTH FLOOR									
ES&T 4303, 4306 & 4304	51	ChBE/ CEE, EAS	4303 Jones 4306 Russell	4	A	6/15/2020	1	0%	
ES&T L2160 (2 story room)	52	ChBE	L2160 Galfond (Teaching Lab)	L2	A	6/22/2020	1	0%	
ES&T Lab 1305 & 1309		ChBE	Vacant	1	A	6/29/2020			
ES&T Fourth Floor As-Built, Docs	53			4	A	6/22/2020	5	0%	
ES&T Fourth Floor Drawing Review & Finalization	58			4	A	7/27/2020	2	0%	
BME BUILDING									
BME Schedule Coordination	28					1/13/2020	1	0%	
BME Lower Level									

